Safer Surfacing Replacement

Period Highlight: 20

Plan | Actual | % Complete
Actual (beyond plan) | % Complete (beyond plan)
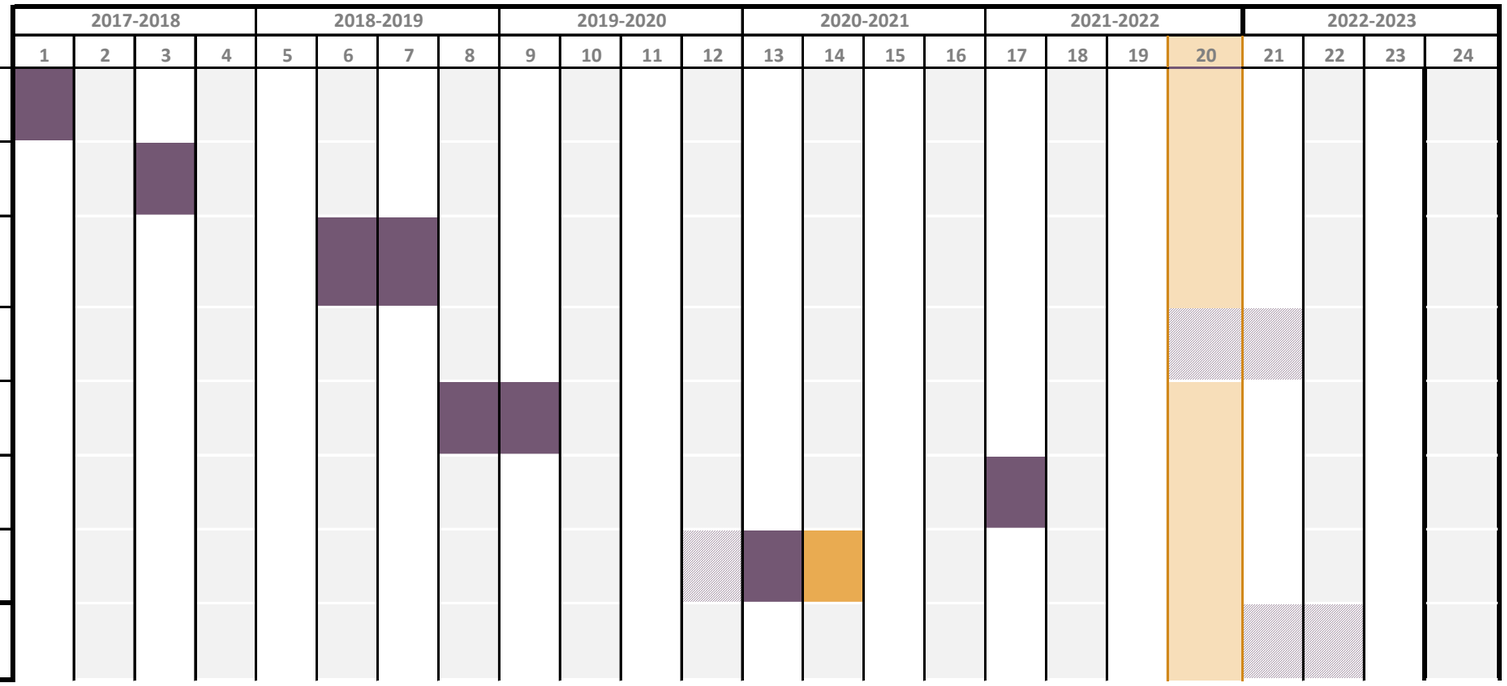
ACTIVITY	PLAN START	PLAN DURATION	ACTUAL START	ACTUAL DURATION	PERCENT COMPLETE
Nicolson Drive	1	1	1	1	100%
Adams Bottom	3	1	3	1	100%
Linslade Recreation Ground	6	2	6	2	100%
Alwins Field	20	2	0	0	0%
Astral Park (Gym)	8	2	8	2	100%
Splash and Play	17	1	17	1	100%
Pages Park	12	2	13	2	100%
Derwent Road	21	2	0	2	0%
